


CITY OF LOS ANGELES
INTERDEPARTMENTAL CORRESPONDENCE

Date: December 1, 2025

To: Street and Transportation Projects Oversight Committee (STPOC)

From: Marcelino Ascensio, PE, Senior Civil Engineer
Architectural Division
Bureau of Engineering 

Subject: **UPDATE OF THE BUREAU OF ENGINEERING MUNICIPAL FACILITIES ARCHITECT, RECREATION AND PARKS (R&P), AND LA RIVER PROJECTS MASTER SCHEDULE AND PROJECT STATUS REPORT**

RECOMMENDATIONS

1. Receive and file the attached updated Municipal Facilities Architect, Municipal Facilities Recreation and Park (R&P), and LA River Projects Master Schedule and Project Status Report.

TRANSMITTALS

1. Updated Municipal Facilities Architect, Municipal Facilities Recreation and Park (R&P), and LA River Projects Master Schedule (Dated December 1, 2025)
2. Updated Project Status Report (Dated December 1, 2025)

DISCUSSION

Adjustments have been made to the Municipal Facilities Architect, Municipal Facilities Recreation and Park (R&P), and LA River Projects Master Schedule and Project Status Report to reflect updates and changes since the prior submission.

If you have questions or require additional information, please contact me at marcelino.ascensio@lacity.org or (213) 485-4787.

MA/ma

cc: Daisy Bonilla, City Administrative Office
Salyna Cun, City Administrative Office
Maria Souza-Rountree, City Legislative Office
Steven Fierce, Bureau of Engineering

STPOC - Project Status Report

As Of 12/1/25

Summary		
Current Status		Construction Vehicle
2 - Design - Active	1	Contractor (Regular Award)
4 - Bid & Award - Active	2	General Services Vendor(s)
5 - Construction - Active	1	Other (Explain in Project Description)
6 - Post-Construction - Active	7	
Total	11	Total 11

Bureau of Engineering - Grant Project - Other - LA River Projects

Project Title	Dept Proj. ID	Scope (Summary)	Estimated Const Cost	Funding	Authorization	Project Status	Current Status	CD(s)	Construction Method	Project Manager	Supporting Departments	Federal Aid ID
1 LA River Way West SF Valley Completion Project (Vanalden Ave. to Balboa Blvd.)	EBIKE2	The objective of this project is to construct a Class I bike path and greenway along the LA River through Vanalden Ave. to Balboa Blvd. The scope of the project also includes: mini-traffic circles in the neighborhoods, landscaping, bio-retention basins, lighting, fencing, and up to six (6) under-crossings through the trapezoidal channel of the LA River.	\$ 60,000,000	ATP: \$18,593,000.00 Deadline - Funds for Construction Only - 6/26/2021 (overdue) C1: \$500,000.00 Deadline - No Desc - 6/30/2020 (Met) CO: \$3,000,000.00 Deadline - No Desc - 12/31/2026 (pending) DWP: \$500,000.00 LT: \$500,000.00 Deadline - No Desc - 12/31/2017 (Met) MMLRF: \$1,500,000.00 Deadline - No Desc - 6/30/2021 (Met) MTA: \$15,000,000.00 Deadline - Funds for Construction Only - 12/31/2026 (pending) Oth: \$5,290,000.00 Deadline - No Desc - 6/30/2026 (pending) RPF: \$1,000,000.00 Deadline - No Desc - 6/30/2020 (Met) SPA: \$300,000.00 Deadline - No Desc - 4/25/2019 (Met)	Nov/25 Anticipated re-bid December 2025 with bids due February 2026	93% Bid & Award (Active)	3, 4, 6	Contractor (Regular Award)	Marcelino Ascensio	Bureau of Engineering; Bureau of Contract Administration; Bureau of Sanitation; Bureau of Street Lighting; Dept of Recreation and Parks; Dept of Transportation		
Total			\$ 60,000,000									

Fund Source	Total Amount	Deadlines	Deadlines Met	Deadlines Overdue	Deadlines Next 12 Months
ATP - Active Transportation Program	\$ 18,593,000	1	0	1	0
C1 - Citywide Infrastructure 100/54/00J077	\$ 500,000	1	0	1	0
CO - County	\$ 3,000,000	1	0	0	0
DWP - Department of Water and Power	\$ 500,000	0	0	0	0
LT - Local Transportation Fund	\$ 500,000	1	1	0	0
MMLRF - Measure M Local Return Fund	\$ 1,500,000	1	1	0	0
MTA - Metropolitan Transportation Authority	\$ 15,000,000	1	0	0	0
Oth - Other	\$ 5,290,000	1	0	0	1
RPF - Recreation and Parks Fund 302	\$ 1,000,000	1	1	0	0
SPA - Stormwater Pollution Abatement Fund	\$ 300,000	1	1	0	0
Total	\$ 46,183,000	9	5	1	1

Bureau of Engineering - Non-Grant Project - LA River Projects

Project Title	Dept Proj. ID	Scope (Summary)	Estimated Const Cost	Funding	Authorization	Project Status	Current Status	CD(s)	Construction Method	Project Manager	Supporting Departments	Federal Aid ID
1 Los Angeles Riverfront Park - Phase III (Orange Line to Balboa)	K291	The project is a Proposition K funded project. The scope of work as described in the Proposition K Bond measure states: "Greening along area of Encino, Sherman Oaks, Studio City." The detailed scope of work is being developed with input from the Department of Recreation and Parks staff and the Local Volunteer Neighborhood Oversight Committee (LVNOC).	\$ 6,500,000	ATP: \$1,880,000.00 Deadline - Construction Only - 6/30/2025 (overdue) CO: \$228,000.00 Deadline - No Desc - 6/30/2026 (pending) Prop K: \$800,000.00 Deadline - No Desc - 6/30/2028 (pending) Total funding: \$2,908,000	Nov/25 See EBIKE2 - LA River Way West SF Valley Completion Project (Vanalden Ave. to Balboa Blvd.)	93% Bid & Award (Active)	6	Contractor (Regular Award)	Marcelino Ascensio			
Total			\$ 6,500,000									

Fund Source	Total Amount	Deadlines	Deadlines Met	Deadlines Overdue	Deadlines Next 12 Months
ATP - Active Transportation Program	\$ 1,880,000	1	0	1	0
CO - County	\$ 228,000	1	0	0	1
Prop K - Proposition K	\$ 800,000	1	0	0	0
Total	\$ 2,908,000	3	0	1	1

Bureau of Engineering - Non-Grant Project - Municipal Facilities Architect

Project Title	Dept Proj. ID	Scope (Summary)	Estimated Const Cost	Funding	Authorization	Project Status	Current Status	CD(s)	Construction Method	Project Manager	Supporting Departments	Federal Aid ID
1 Crenshaw Blvd Prop 1C Grant	G1066	The scope of work includes improvement of infrastructure on Crenshaw Blvd. consist of curb ramps, sidewalks, curbs, gutters, pedestrian crossings, street trees, landscaping, cultural art work, planters, and pruning trees and roots by GSD, street median work by BSS, and transit shelter removal and installation by OFJCD. Design process is included in the construction phase. The work within CD 6 only includes the installation of bus shelters by BSS.	\$ 7,279,568	CRA: \$7,279,568.00 Deadline - Prop 1C Grant Deadline extended. All invoices must be submitted by 5/30/22. - 6/30/2022 (overdue) Total funding: \$7,279,568.00	Jun/25 The project was completed in September of 2024. The Project closeout was extended due to the development of As Built drawings for LADOT.	74% Post-Construction (Active)	8, 10	General Services Vendor(s)	Ohaji Abdallah			
2 Destination Crenshaw	G1133	Destination Crenshaw project is a 1.3-mile long outdoor art and culture experience celebrating Black Los Angeles. BOE's involvement is to act as the Grant Administrator for the Destination Crenshaw project, and the procurement of design consultant services.	\$ 22,323,000	GF: \$1,500,000.00 Oth: \$14,500,000.00 PVT: \$20,500,000.00 ST: \$10,000,000.00 Total funding: \$46,500,000.00	Aug/25 Destination Crenshaw has not remobilized. Per CD 8 request, BOE is working on Council Report to obtain authorization to accept MAT funds to pass through to Destination Crenshaw, the non-profit, to complete the tunnel lid crossing intersection.	94% Construction (Active)	8	Other (Explain in Project Description)	Joanne J. Zhang	Bureau of Engineering; Bureau of Contract Administration; Board of Public Works; City Administrative Officer; Council/CLA		
3 Evergreen Park Street Enhancement Project (LAN)	G1076	Project consist of installation of new continental crosswalks at 17 intersections (46 legs total), sixty-eight (68) new street trees, Bus Stop Security Lighting of 3 per bus stop (19 total), Bus Shelters (3 total), Bus Benches (4 total) and Curb Ramps (6 total).	\$ 755,000	TGF: \$748,716.00 Total funding: \$748,716.00	Oct/25 BCA is working on close out board report.	74% Post-Construction (Active)	14	Contractor (Regular Award)	Guillermo Barragan			
4 Sheldon Arleta Park - Arleta Ave. Street Improvement	K361	The scope of work is to construct acceleration and deceleration lanes, left turn lane, traffic signal, pedestrian crossing signal, sidewalk, curb, gutter, street trees, street lights, relocate fire hydrants, to relocate utility poles, construct fence, ADA ramps at street corners, irrigation, landscaping, and street signage.	\$ 2,810,625	ST: \$3,075,000.00 Total funding: \$3,075,000.00	Nov/25 Motion has been approved to relocation the funds to pay outstanding invoices. (CL)	5% Post-Construction (Active)	6	Contractor (Regular Award)	Chelsea Li	Bureau of Engineering; Bureau of Contract Administration; Bureau of Sanitation; Bureau of Street Lighting; Dept of Recreation and Parks; Bureau of Street Services		

5	Sheldon Arieta Park - Sharp Ave	K364	The scope of work is to construct traffic lanes, traffic signal, pedestrian crossing signal, sidewalk, curb, gutter, street trees, street lights, relocate fire hydrants, relocate utility poles, construct fence, ADA ramps at street corners, irrigation, landscaping, and street signage.	\$ 1,311,028	Oth: \$289,882.00 ST: \$2,843,734.00 Total funding: \$3,133,716.00	Nov/25 The updates are shown on K361. (CL)	82% Post-Construction (Active)	6	Contractor (Regular Award)	Chelsea LI	Bureau of Engineering, Bureau of Contract Administration, Bureau of Sanitation, Bureau of Street Lighting, Dept of Recreation and Parks, Bureau of Street Services	
6	Sheldon Arieta Park - Sheldon Street	K363	The scope of work is to construct traffic signal, pedestrian crossing signal, sidewalk, curb, gutter, street lights, relocate guy wires, relocate utility poles, construct fence, ADA ramps at street corners, and street signage.	\$ 2,700,000	Oth: \$1,974,614.00 ST: \$883,385.00 Total funding: \$2,857,999.00	Nov/25 The consultant is revising the plans. (CL)	99% Design (Active)	6	Contractor (Regular Award)	Chelsea LI	Bureau of Engineering, Dept of Recreation and Parks, Bureau of Street Services	n/a
7	Sheldon Arieta Park - Wicks Street	K362	The scope of work is to construct traffic lanes, traffic signal, pedestrian crossing signal, sidewalk, curb, gutter, street trees, street lights, relocate fire hydrants, relocate utility poles, construct fence, ADA ramps at street corners, irrigation, landscaping, and street signage.	\$ 2,029,949	MMLRF: \$1,420,270.00 ST: \$1,120,730.00 Total funding: \$2,541,000.00	Nov/25 K361 has the updates. (CL)	82% Post-Construction (Active)	6	Contractor (Regular Award)	Chelsea LI	Bureau of Engineering, Bureau of Contract Administration, Bureau of Sanitation, Bureau of Street Lighting, Dept of Recreation and Parks, Bureau of Street Services	
8	Westlake MacArthur Park Pedestrian Improvements	G1060	Design and construction of 2.5 miles of pedestrian enhancements including 33 new pedestrian security lights, 22 bus benches, 22 trash receptacles, 85 street trees, continental crosswalks (10 locations), curb ramps (4 locations), landscape medians, irrigation and one year maintenance period.	\$ 1,154,333	CMAQ: \$1,339,386.00 PropC: \$334,847.00 Total funding: \$1,674,233.00	Oct/25 ConAd will work on final Close out Board Report.	62% Post-Construction (Active)	1	Contractor (Regular Award)	Guillermo Barragan		
8	Total			\$ 40,363,501								


Fund Source	Total Amount	Deadlines	Deadlines Met	Deadlines Overdue	Deadlines Next 12 Months
CMAQ - Congestion Mitigation and Air Quality	\$ 1,339,386	0	0	0	0
CRA - Community Redevelopment Agency	\$ 7,278,568	1	1	0	0
GF - General Fund	\$ 1,500,000	0	0	0	0
MMLRF - Measure M Local Return Fund	\$ 1,420,270	0	0	0	0
Oth - Other	\$ 16,764,596	0	0	0	0
PropC - Proposition C	\$ 334,847	1	1	0	0
PVT - Private or other agency	\$ 20,500,000	0	0	0	0
ST - State Fund	\$ 17,722,849	0	0	0	0
TGF - Transportation Grant Fund	\$ 748,716	0	0	0	0
Total	\$ 67,610,232	2	1	1	0

Bureau of Engineering - Non-Grant Project - Municipal Facilities R and P

Project Title	Dept Proj ID	Scope (Summary)	Estimated Const Cost	Funding	Authorization	Project Status	Current Status	CD(s)	Construction Method	Project Manager	Supporting Departments	Federal Aid ID
1 Mid Valley IGMPK Park Public Works Improvements	K335	to improve 200 feet of side walk, curb ,gutter and street	\$ 367,313	C1: \$101,161.00 Deadline - No Desc - 4/5/2021 (Met) CDBG: \$375,000.00 Deadline - No Desc - 7/7/2017 (Met) Total funding: \$476,161.00		Oct/25 PW Board Report being Process. Sep/25 PW Board Report being Process. Aug/25 PW Board Report being Process. Jul/25 PW Board Report being Process. Jun/25 PW Board Report being Process.	95% Post-Construction (Active)	6	Contractor (Regular Award)	Raymundo Araujo		CDBG N143-23
Total			\$ 367,313									

Fund Source	Total Amount	Deadlines	Deadlines Met	Deadlines Overdue	Deadlines Next 12 Months
C1 - Citywide Infrastructure 100541003077	\$ 101,161	1	1	0	0
CDBG - Community Development Block Grant	\$ 375,000	1	1	0	0
Total	\$ 476,161	2	2	0	0

Fund Source	Total Amount	Deadlines	Deadlines Met	Deadlines Overdue	Deadlines Next 12 Months
ATP - Active Transportation Program	\$ 20,473,000	2	0	2	0
C1 - Citywide Infrastructure 100541003077	\$ 691,161	2	2	0	0
CDBG - Community Development Block Grant	\$ 375,000	1	1	0	0
CMAQ - Congestion Mitigation and Air Quality	\$ 1,339,386	0	0	0	0
CO - County	\$ 3,228,000	2	0	0	1
CRA - Community Redevelopment Agency	\$ 7,278,568	1	0	1	0
DWP - Department of Water and Power	\$ 500,000	0	0	0	0
GF - General Fund	\$ 1,500,000	0	0	0	0
LT - Local Transportation Fund	\$ 500,000	1	1	0	0
MMLRF - Measure M Local Return Fund	\$ 2,920,270	1	1	0	0
MTA - Metropolitan Transportation Authority	\$ 15,000,000	1	0	0	0
Oth - Other	\$ 22,054,596	1	0	0	1
Prop K - Proposition K	\$ 800,000	1	0	0	0
PropC - Proposition C	\$ 334,847	1	1	0	0
PVT - Private or other agency	\$ 20,500,000	0	0	0	0
RPF - Recreation and Parks Fund 302	\$ 1,000,000	1	1	0	0
SPA - Stormwater Pollution Abatement Fund	\$ 300,000	1	1	0	0
ST - State Fund	\$ 17,722,849	0	0	0	0
TGF - Transportation Grant Fund	\$ 748,716	0	0	0	0
Total	\$ 117,177,393	16	8	3	2

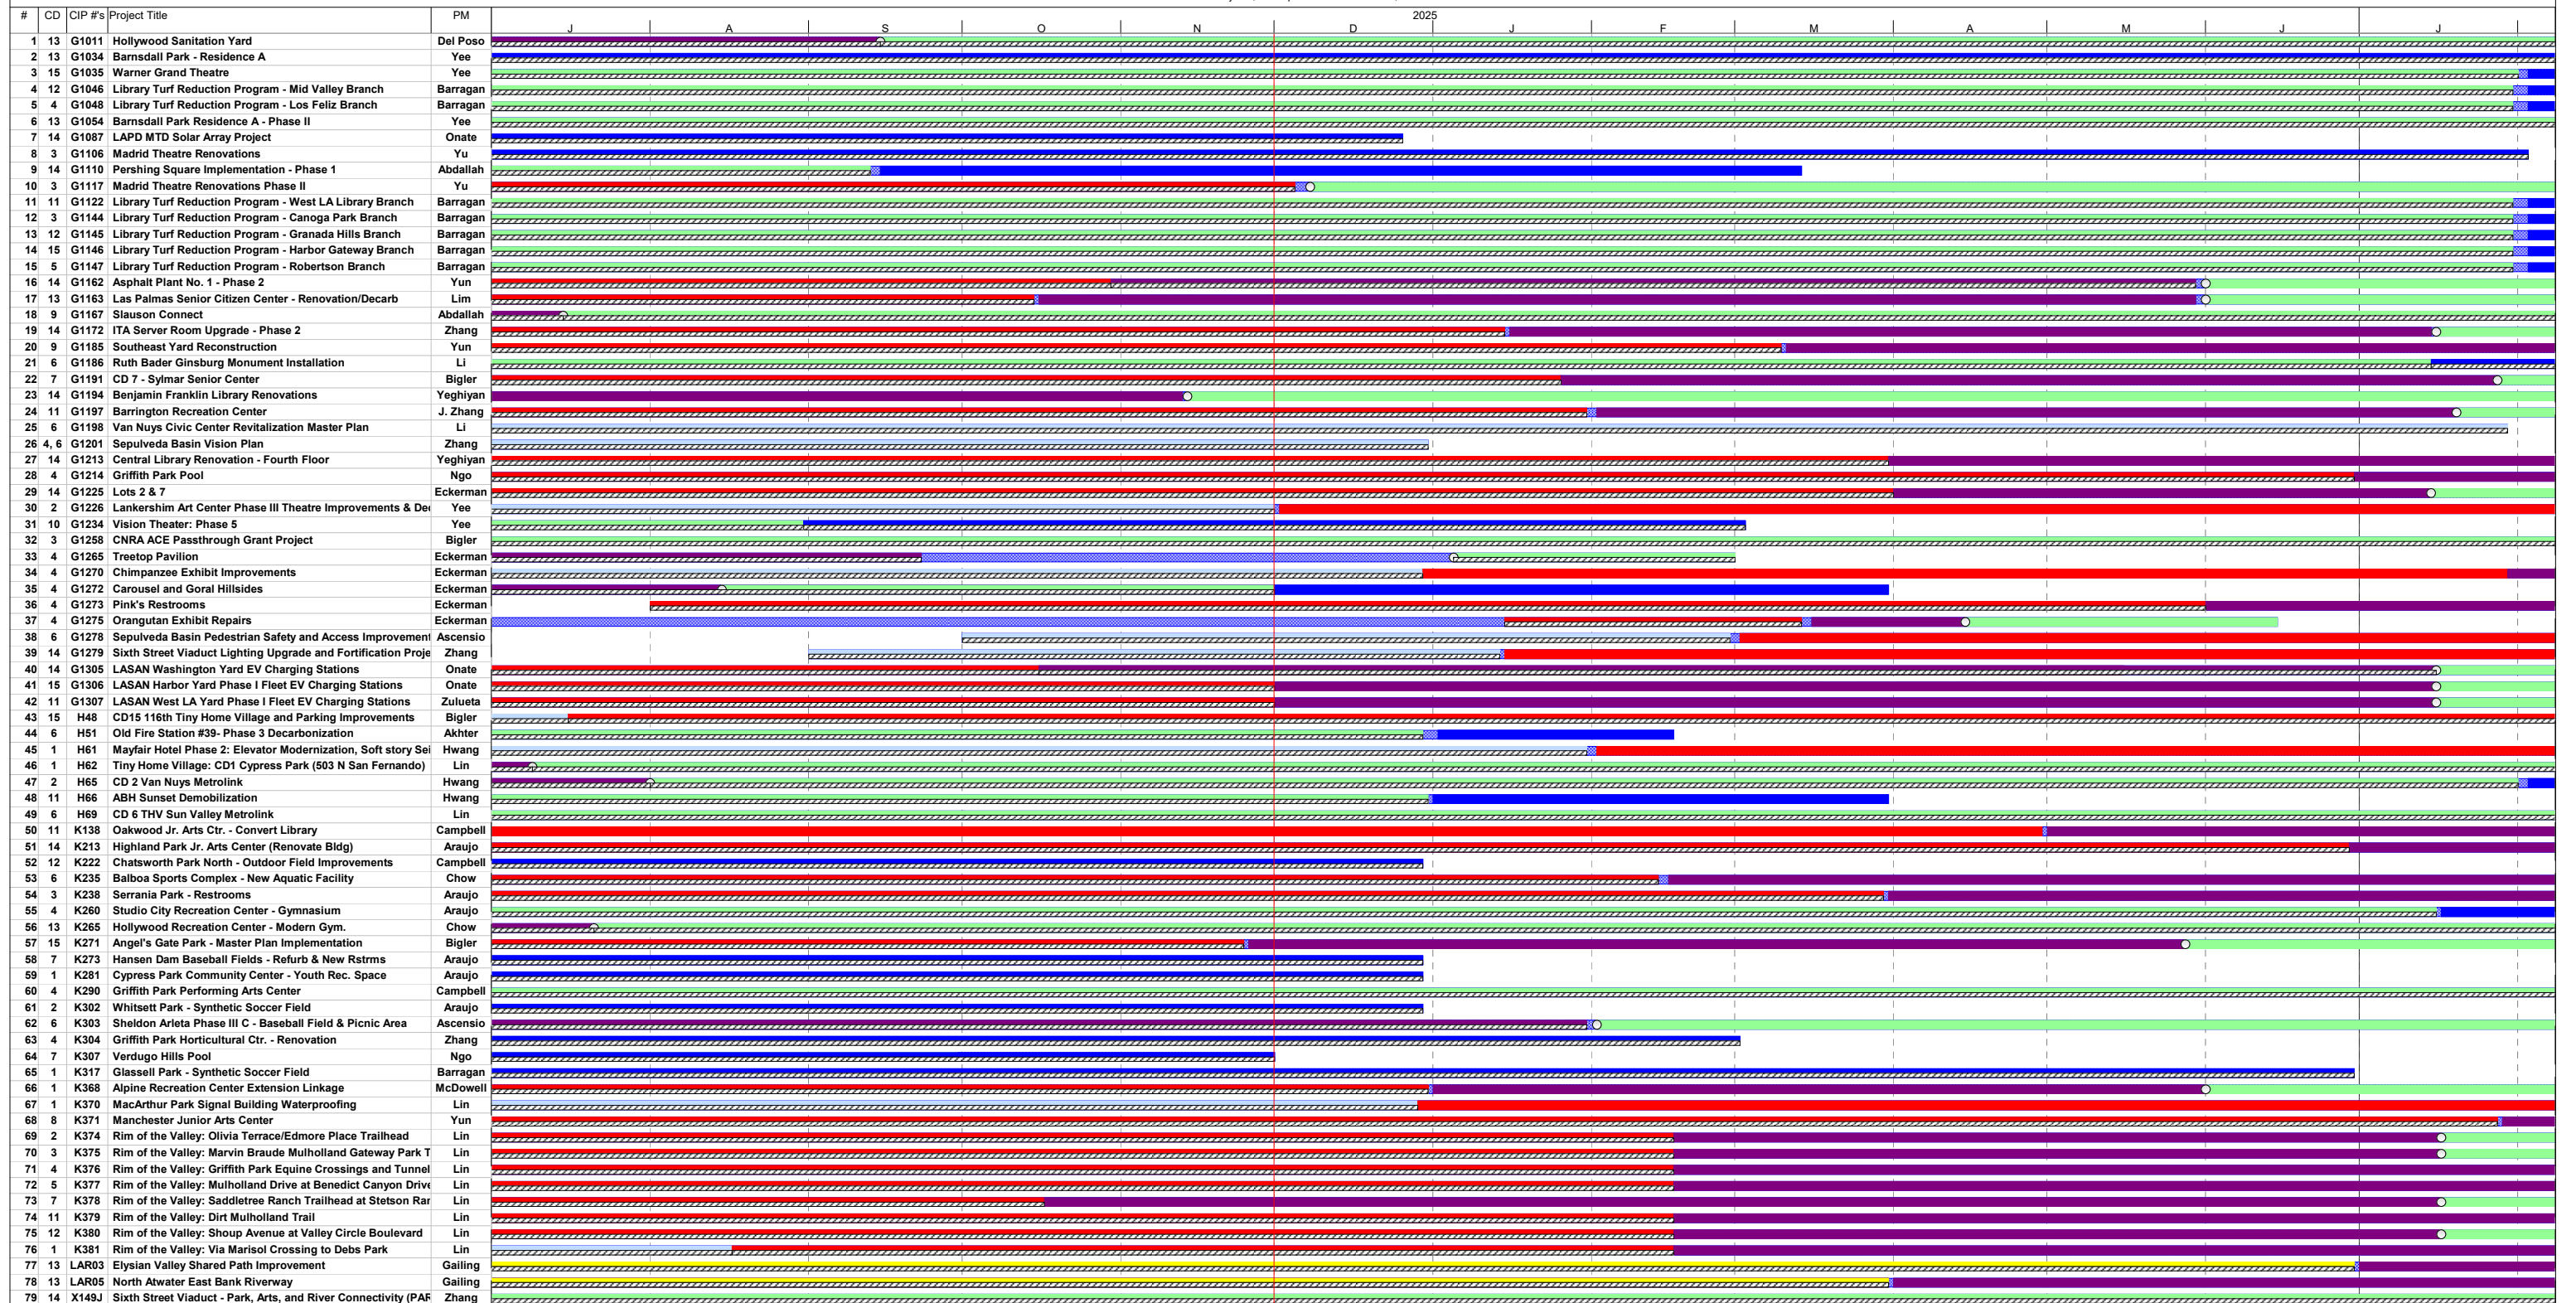

Project: Master Schedule (UPRS)
Date: Mon 12/1/25

Task		PreDesign		Cons		External Milestone		Inactive Milestone		Manual Task		Manual Summary		External Tasks		External Milestone	
Split		Design		PostCons		Deadline		Inactive Milestone		Duration-only		Start-only		External Milestone		External Milestone	
Milestone		BidAward		RightOfWay		Inactive Task		Inactive Summary		Manual Summary Rollup		Finish-only		Progress		External Milestone	
